



# Standard Procurement System

---

***Presented By:***

***Kathy Jenkins***

***June 28, 2000***

- A **JOINT** standard automated process system which is data based and data managed
- A component of a DoD enterprise business system
- One of the systems allowing for the replacement of MOCAS

- Reduce unmatched disbursements
- Single automated system for Procurement
- Reduce legacy systems
- Enable productivity
- Achieve paperless contracting
- Achieve Procurement-Finance To-Be Model

# Moving from MOCAS

**MOCAS currently performs 14 major functions**

## In MOCAS

Access Financial Information  
Access Delivery Information  
Process Shipment/Acceptance  
Entitlement  
Electronic Contract Closeout  
Provide Financing Payment  
Information

**DPPS/DCD/DCW**

**WAWF**

## MOCAS Non-Core

QA-MIS  
Track Property System Approval  
Contract Audit Follow-up  
Deficiency Tracking (PQDR)

**SPS**

## Direct MOCAS Interface

Contract Modifications  
Management Information  
Electronic Payment Processing


**SIS**

## Indirect MOCAS Interface

Delivery Status (ALERTS)

*... which  
will  
migrate to  
a variety  
of new  
and  
existing  
systems*

# Putting it together

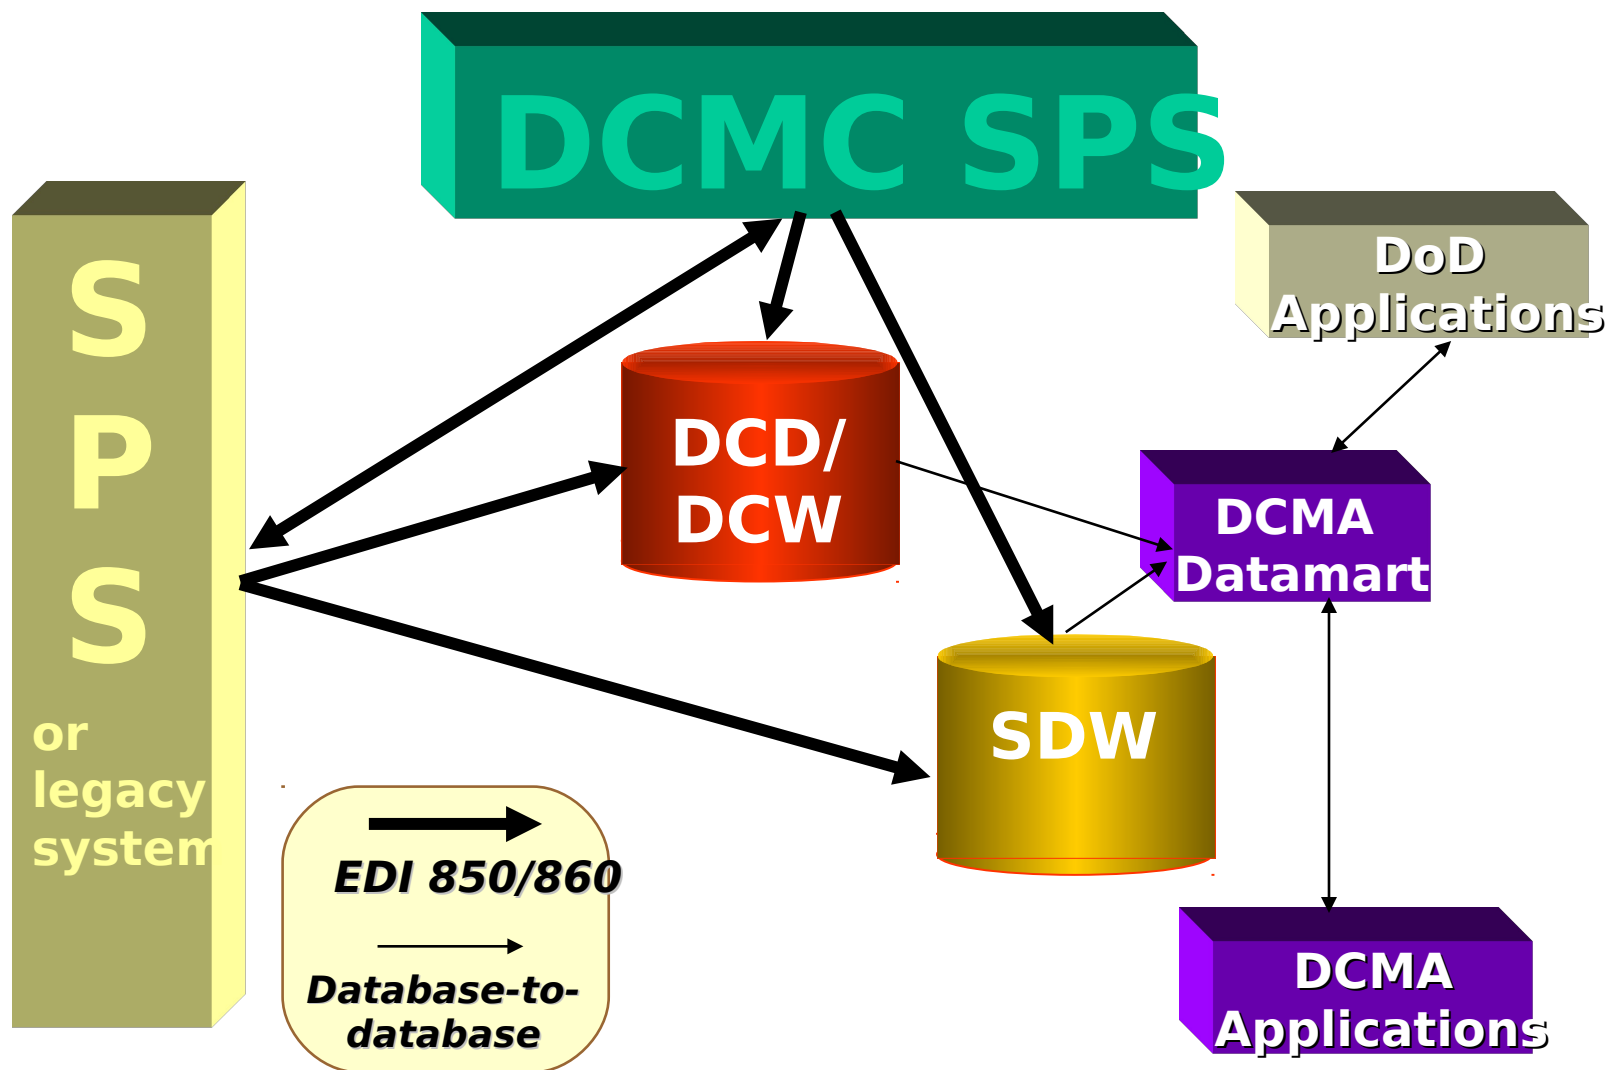

# SPS Deployment Path

Nov 99 — May 00 Jun 00 Jul 00 Aug 00 Sep 00 Oct 00 Nov00 Dec 00 Jan 01 Feb 01 Mar 01 Apr 01 May01 June 01 Jul

**Version 4.1**  
*Replace  
purchasing  
systems*

**SACONS**

**BOSS**

**Version 4.2**

**Initial Planning**

**PFX**

**ET/OT**

**PILOTS**

**DEPLOYMENT**

**Testing**

**Testing**

**Testing**

**Testing**

**4.2 BETA  
April 28**

**SPS-I  
BETA (R1)  
5 July**


**SPS-I  
BETA (R2)  
11 Sep**

**V4.2  
22  
Dec**

**SPS-I  
V4.2  
15 Jan**

# Progress To Date...

- ✓ **Phase I Planning completed 31 May**
  - Developed Detailed Training and Deployment Plans
  - Detailed DCMA Business Processes Defined
- ✓ **Infrastructure Analysis briefed to DCMA CIO**
- ✓ **SPS-I (EDI Interfaces) ongoing development/IRD Review**

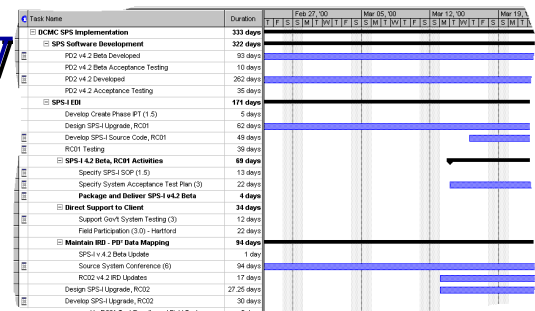

- ✓ **9 Focus Groups with Process Owners and DCMA Field Reps**  
held to identify standard business processes
- ✓ **Utilized DCMA One Book as basis for processes**
- ✓ **Contract Closeout and Modifications “Must Do”**
- ✓ **16 other business processes being considered for SPS including:**
  - ▣ **Contract Receipt & Review**
  - ▣ **Terminations**
  - ▣ **Negotiations**
  - ▣ **Property Administration**





# ***Detailed Training Plan***

After careful analyses of the DCMA user population, the following training will be required for V4.2:

- ✓ **Contract Administration**  
3845 users  
330 classes
- ✓ **Management Overview**  
696 users  
58 classes
- ✓ **System Administration**  
140 users  
12 classes



***To expedite training, DCMA has elected to conduct training at 80 different CompUSA training facilities nationwide.***

***Teaming AMS trainers with DCMA functional specialists***

- **Performance Force Exercise (PFX)**

***Process owners and field reps will develop and evaluate procedures for using SPS to perform DCMA business processes (July10-August 31)***

- **Field Validation (ET/OT)**

***Field users will simulate using SPS to evaluate policies, procedures, training, infrastructure and deployment methods (October 16-November 17)***

- **Pilot Deployments**

***Final proof of the deployment process. Pilots Hartford, Santa Ana, LM Orlando, Boeing Seattle (March-April 2001)***

- It will have a major impact on how we do business.
- SPS will not just be a tool for doing our job, it will be the way we do the job.
- Contractor provided training, leased facilities and aggressive schedule mean one chance at training.
- But...

*The training*

*the equipment*

*the policies and procedures*

*the support...will all be in place*

- **FST members have been key participants in all activities so far**
- **There will be expanding participation as we move through the phase II events**
- **The FST will be critical through deployment and post deployment**

***Supporting training (approximately 40 training teams required)***

***Supporting the field as they transition to new systems and new business processes***

***In expediting communication on issues and resolution***
